



Update on FCPS Construction/Renovation Projects

July 2018



New Elementary at Athens-Boonesboro

▶ Architect:	EOP Architects
▶ General Contractor:	Griggs Enterprises
▶ GC Contract Sum:	\$17,860,200
▶ Total Project Cost:	\$23,801,841
▶ Change Orders to Date (2):	\$94,362.93
▶ Scheduled Contract Completion Date:	July 2019
▶ % of Contract Completed:	10.34 %
▶ Revised Completion Date per GC:	No Change

New Elementary at Athens-Boonesboro

Schematic Rendering of Final Façade



New Elementary at Athens-Boonesboro

▶ **Work Completed to Date (June):**

Sector C: Continue interior footers

- ▶ Complete Underground MEP
- ▶ Kitchen rough-in complete
- ▶ Start structural masonry
- ▶ Door frames begun

Sector D: Perimeter Foundations continued


- ▶ Underground MEP is complete
- ▶ Dock area excavation continued

Sector E: Perimeter Foundations complete

- ▶ Interior Foundations have started
- ▶ Underground MEP is complete

Outside building pad:

- ▶ Continue grading outside of building pad
- ▶ Continue forced main and lift station install
- ▶ Begin Storm drainage

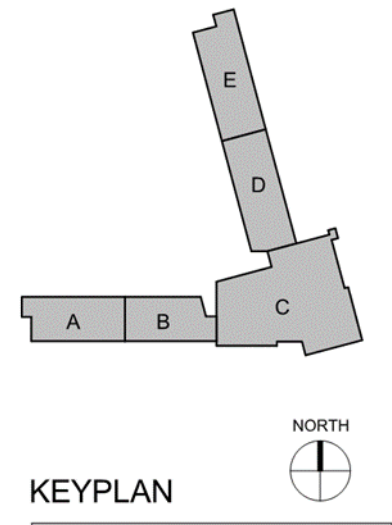

New Elementary at Athens-Boonesboro

▶ **Current Work Effort (July):**

Sector A:

- ▶ Foundation walls
- ▶ Start underground MEP

Sector B:

- ▶ Foundation walls
- ▶ Start underground MEP

Sector C:

- ▶ Continue Masonry
- ▶ Continue Door frames
- ▶ Slabs

▶ **Sector D:**


- ▶ Complete underground MEP and Slabs

Sector E:

- ▶ Complete underground MEP and Slabs

Outside building pad:

- ▶ Continue with storm

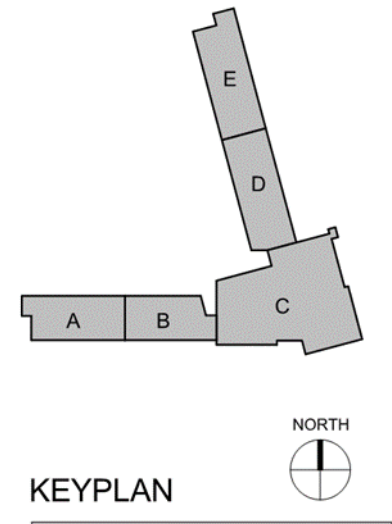

New Elementary at Athens-Boonesboro

Kitchen Rough-in



Structural Masonry



Perimeter Foundations (D)



Dock Area Excavation



New Elementary at Athens-Boonesboro

Interior Foundations (E)



Playground Area



Parent Loop (Looking West)

