



Update on FCPS Construction/Renovation Projects

May 2018



New Elementary at Athens-Boonesboro

▶ Architect:	EOP Architects
▶ General Contractor:	Griggs Enterprises
▶ GC Contract Sum:	\$17,860,200
▶ Total Project Cost:	\$23,801,841
▶ Change Orders to Date (0):	\$0
▶ Scheduled Contract Completion Date:	July 2019
▶ % of Contract Completed:	<1.0%
▶ Revised Completion Date per GC:	No Change

New Elementary at Athens-Boonesboro


Schematic Rendering of Final Façade



New Elementary at Athens-Boonesboro

▶ **Work Completed to Date:**


- ▶ All lime stabilization has been accomplished beneath the building pad
- ▶ Complete soil lifts for all sectors
- ▶ Foundations have been started ahead of schedule for Sector C - the central section of the school: gym, admin, cafeteria, media center
- ▶ Begin monitoring of settlement plates for classroom wings
- ▶ Grading beyond building pad has begun
- ▶ Exterior wall mockup is under construction and review
- ▶ Additional drive lane was completed at construction entrance

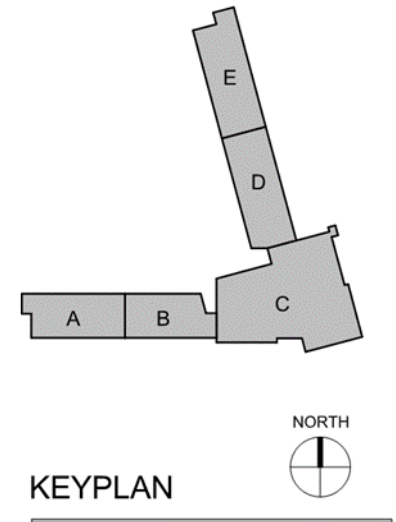

New Elementary at Athens-Boonesboro

▶ **Current Work Effort (May):**

- ▶ Continued settlement monitoring for both classroom wings
- ▶ Continue grading outside building pad
- ▶ Sector C: Continue foundations, place underground mechanical/electrical, install 1st course of CMU on interior footers, & start placing gravel for slab
- ▶ Start installation of Lift Station & Forced Main
- ▶ Start footers/foundation walls Sector D/E

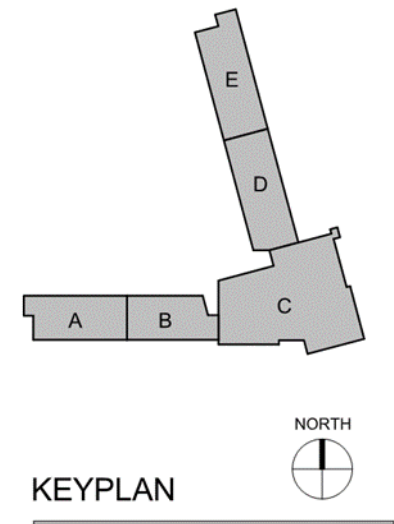

New Elementary at Athens-Boonesboro

Foundations – Sector C



Foundations – Sector C



Final Lifts – Sector A



Sector A – Seen from Hwy.



New Elementary at Athens-Boonesboro

Site Mtg. w/ Geotech



Playfield Area



Exterior Wall Mockup



Mockup w/ Air & Vapor Barriers

